

Agile Backlog Creation & Sprint Simulation in Jira

Digital Campus Library Reservation Gateway (DCLG)

Name	Kushal G
SRN	PES1UG24AM145
Section	C
Assignment	Lab 2 - Jira
Team	Team 08 - Problem Statement #08
Team member / Epic	Kushal G - Overdue Fine Management

Contents

1. Epic, User Stories and Story Points
2. Sprint Execution
3. Sprint Report and Burndown Chart
4. Reflection Questions

1. Epic, User Stories and Story Points


Epic DCLG-1 Overdue Fine Management has 3 user stories totalling 13 story points (Fibonacci scale). The stories cover automatic fine calculation and posting, viewing outstanding fine transactions, and online payment with balance restoration.

Priority was kept at High for all three stories because the overdue-fine flow directly affects a member's account balance and borrowing privileges. Story points were assigned relatively using complexity, effort and uncertainty.

Key	User Story	Priority	Story Points
DCLG-3	Automatically Calculate and Post Overdue Fines	High	5
DCLG-4	View Outstanding Fine Transactions	High	3
DCLG-5	Pay Overdue Fines	High	5
Total	3 stories		13

Story scope

DCLG-3 implements the FR-003 overdue-fine flow. DCLG-4 covers the display of outstanding fine transactions and amounts. DCLG-5 covers online payment, ledger update and restoration of borrowing privileges when the balance reaches zero, while the declined-payment path leaves the balance unchanged and allows retry.

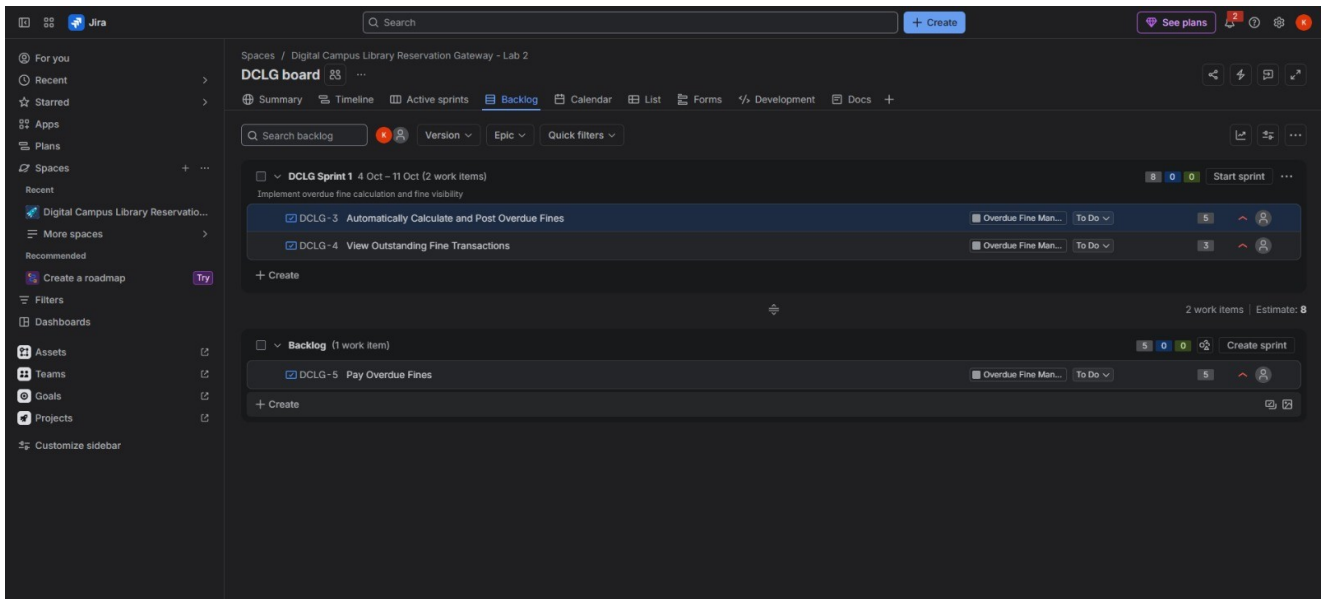Figure 1.1: Backlog - Stories with Priority, Story Points and Parent Epic

Backlog view with Sprint 1 containing DCLG-3 (5 points) and DCLG-4 (3 points), while DCLG-5 (5 points) remains in the backlog. All three stories are linked to the Overdue Fine Management epic.


2. Sprint Execution

Sprint	Stories	Epic	Points	Sprint Goal	Result
Sprint 1 4 Oct - 11 Oct	DCLG-3, DCLG-4 (2 stories)	Overdue Fine Management	8	Implement overdue fine calculation and fine visibility	2 of 2 Done
Sprint 2 11 Oct - 18 Oct	DCLG-5 (1 story)	Overdue Fine Management	5	Implement overdue fine payment and balance restoration	1 of 1 Done
Total	3 stories	1 epic	13		All Done

Both sprints were configured as one-week Scrum sprints and are presented as week-long sprint executions. The planned work was tracked from sprint start to completion within each one-week time-box.


Sprint 1 (Figures 2.1 and 2.2)

Figure 2.1: Sprint 1 - Active Board at Start

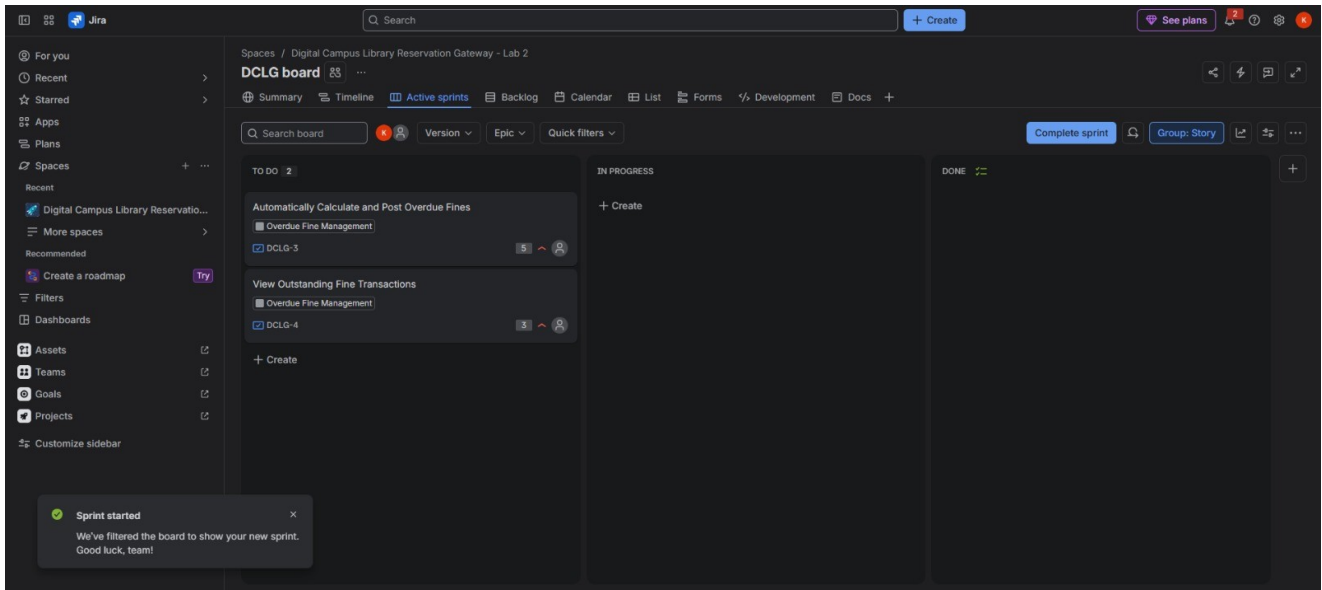

Sprint 1 active board with DCLG-3 and DCLG-4 initially in To Do. Total committed work: 8 story points.


Figure 2.2: Sprint 1 - Active Board (completed)

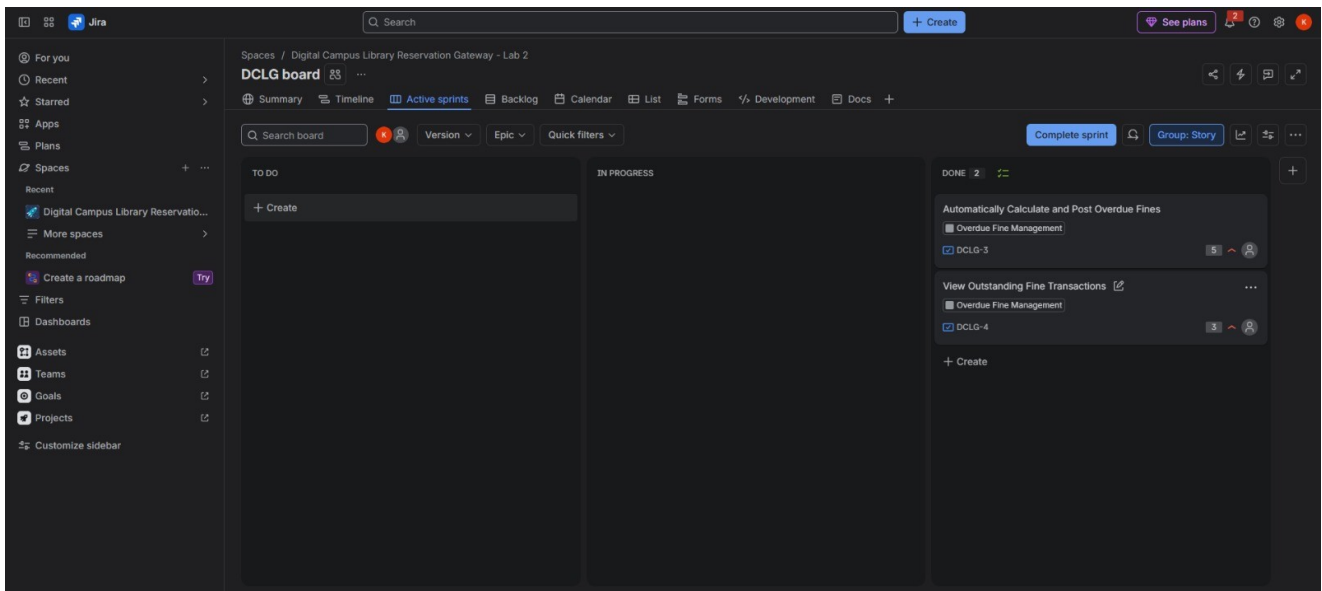

Both committed stories, Automatically Calculate and Post Overdue Fines and View Outstanding Fine Transactions, are in Done. Sprint 1 delivered all 8 committed points.


Sprint 2 (Figures 2.3 and 2.4)

Figure 2.3: Sprint 2 - Active Board at Start

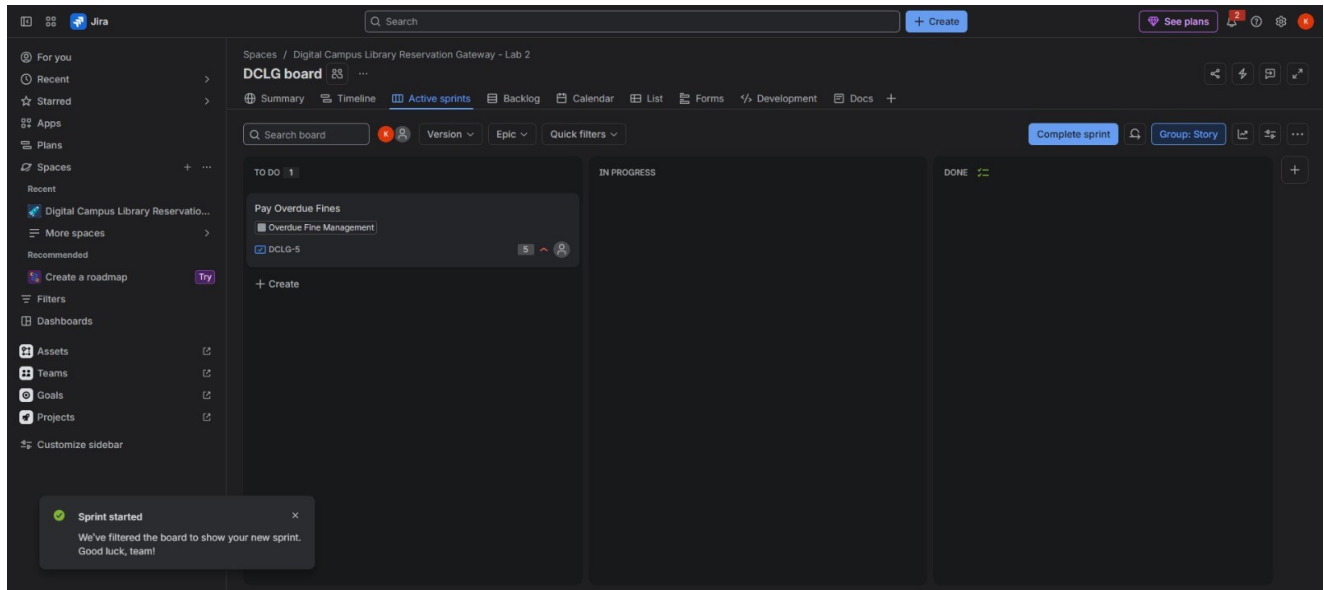

Sprint 2 active board with DCLG-5 Pay Overdue Fines initially in To Do. Total committed work: 5 story points.

Figure 2.4: Sprint 2 - Active Board (completed)

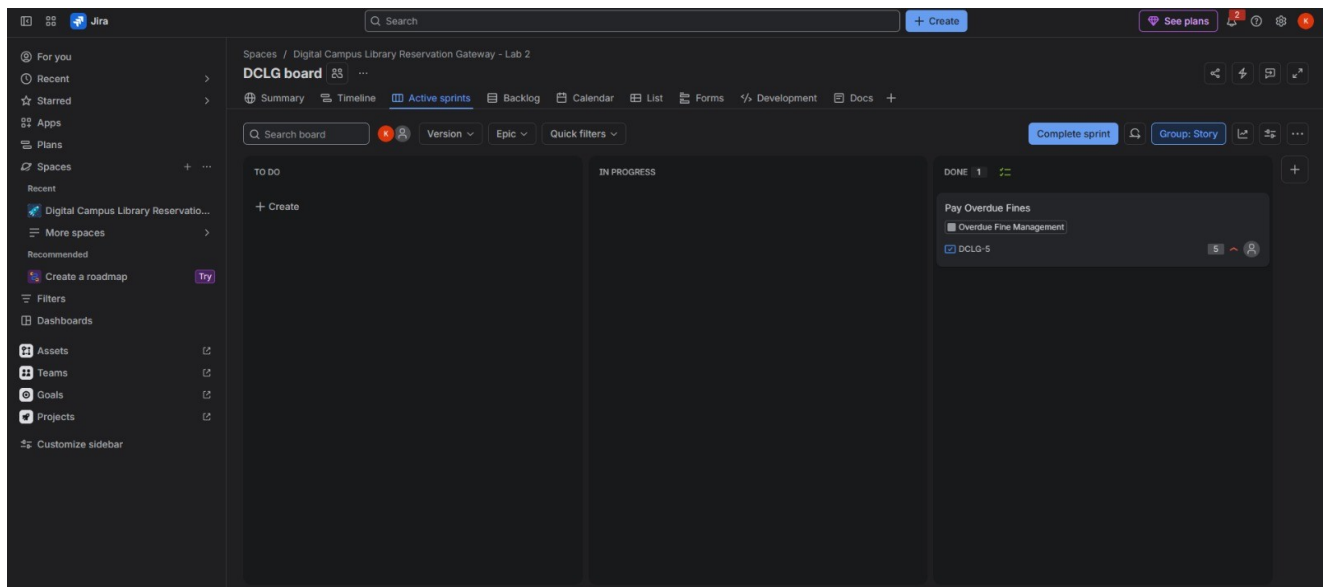


DCLG-5 Pay Overdue Fines is in Done, with To Do and In Progress empty. Sprint 2 delivered all 5 committed points.

3. Sprint Report and Burndown Chart


Sprint 1 - Report and Burndown

Figure 3.1: Sprint 1 Sprint Report

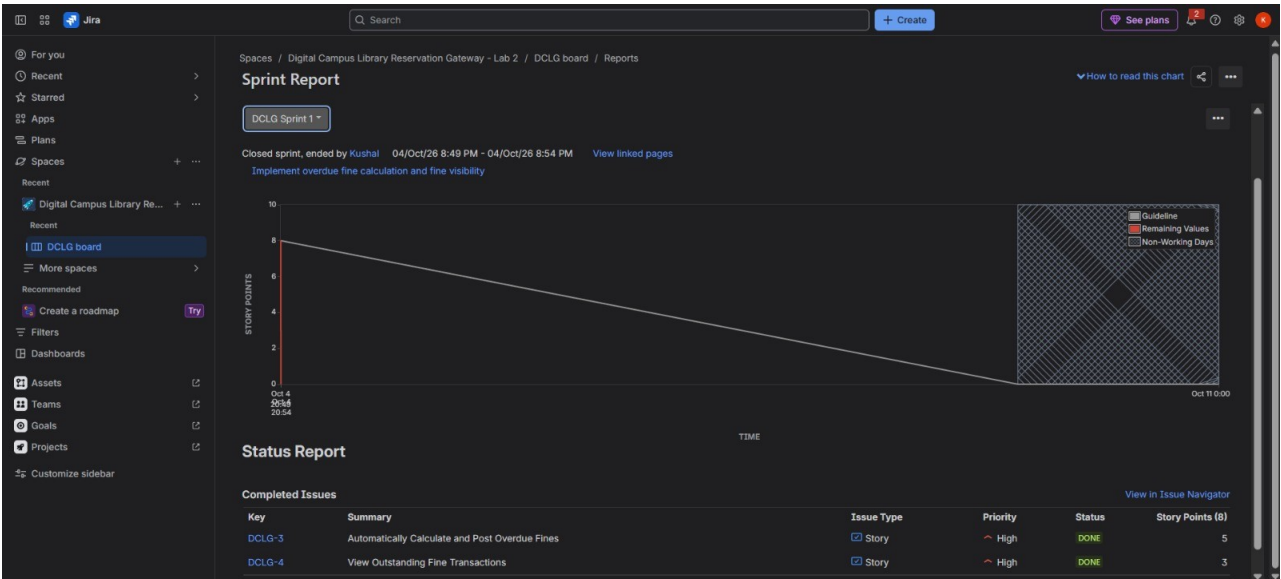

Sprint 1 report shows the goal, 8 completed story points, and both committed stories in Done. The remaining work reaches zero within the sprint time-box, indicating completion of the committed plan.

Figure 3.2: Sprint 1 Burndown Chart (story points)

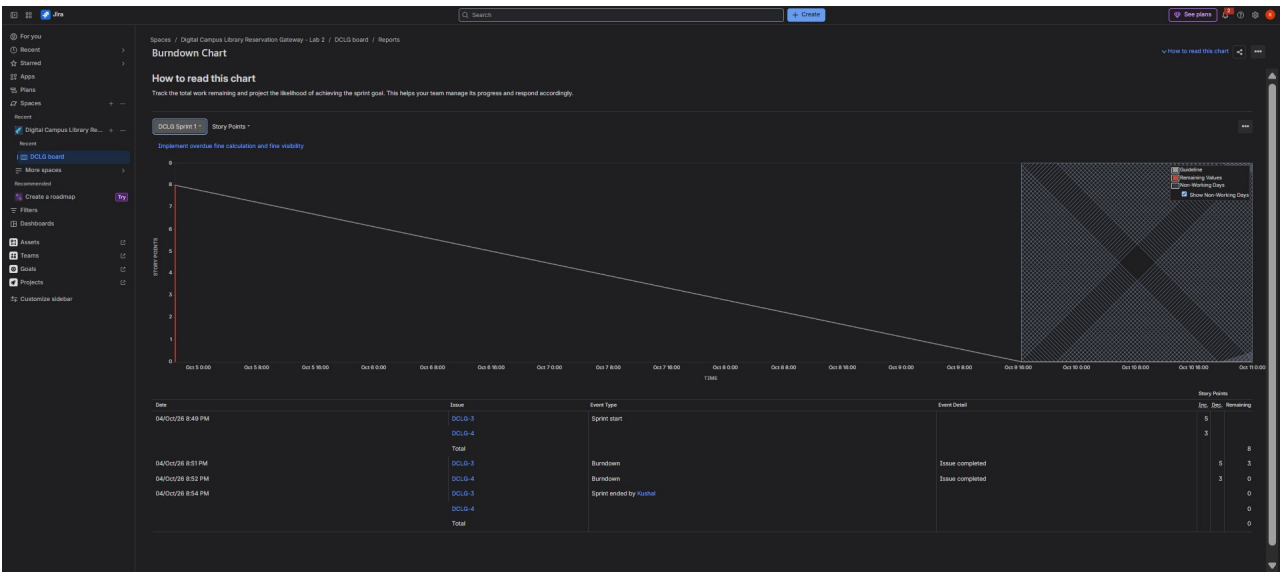


Sprint 1 burndown starts at 8 points and reaches 0 after DCLG-3 and DCLG-4 are completed, confirming that all committed work was delivered within the sprint time-box.

3. Sprint Report and Burndown Chart (continued)


Sprint 2 - Report and Burndown

Figure 3.3: Sprint 2 Sprint Report

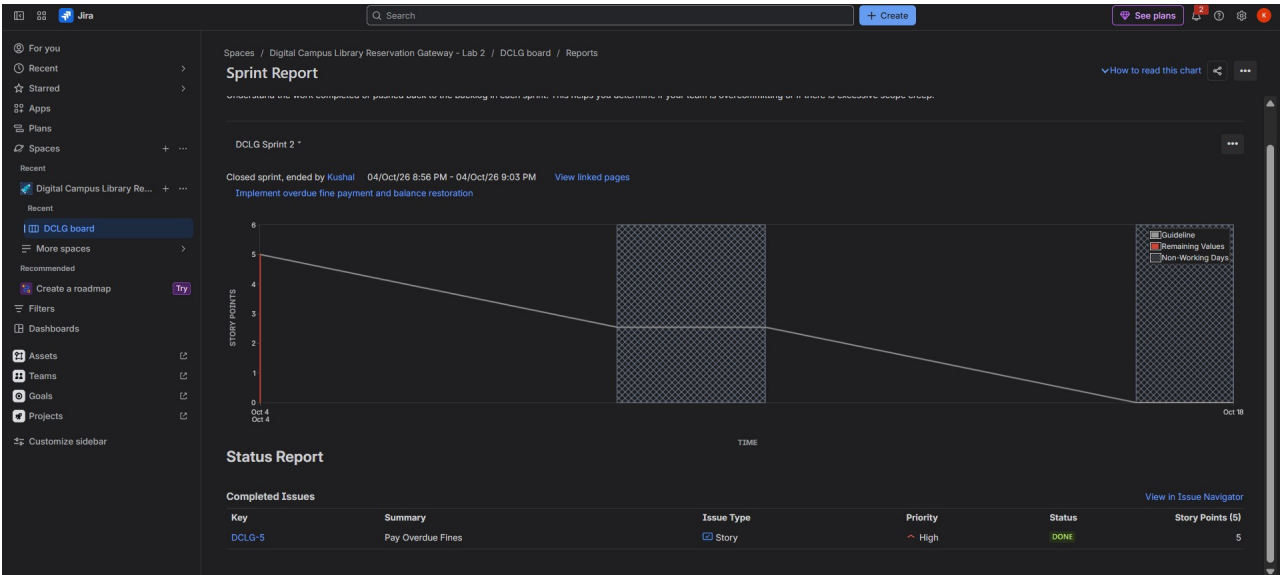

Sprint 2 report shows the payment-and-restoration goal, DCLG-5 in Done, and 5 completed story points.

Figure 3.4: Sprint 2 Burndown Chart (story points)

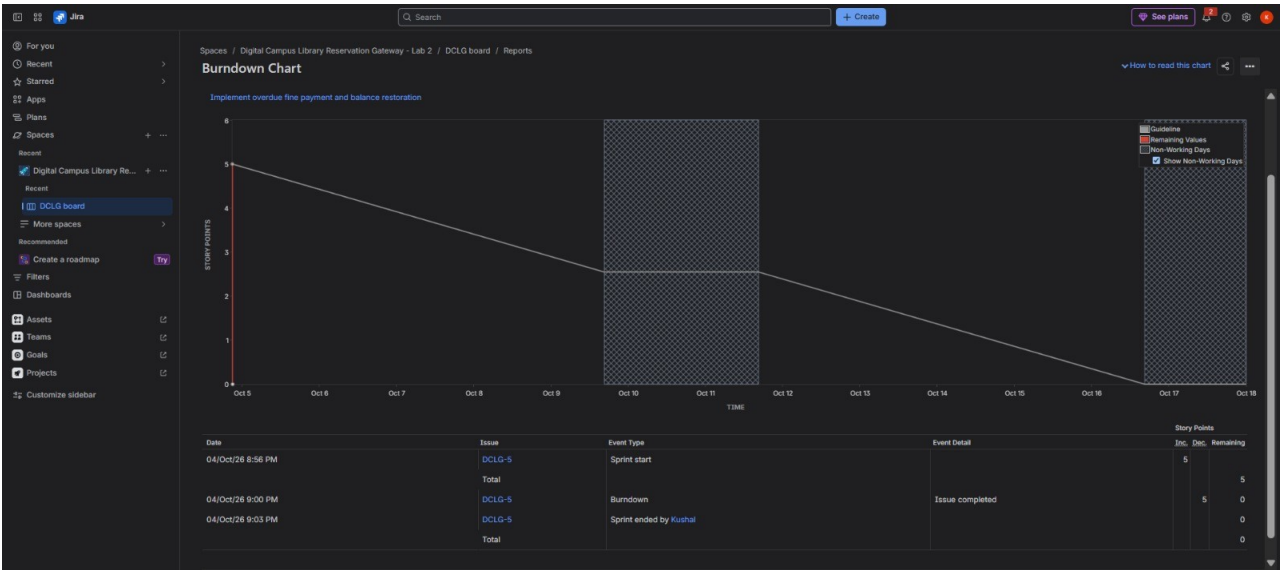

Sprint 2 burndown starts at 5 points and reaches 0 after DCLG-5 is completed, confirming that the full committed workload was delivered within the sprint time-box.

4. Reflection Questions

1. Did your estimations reflect the actual effort?

Yes. The estimates reasonably reflected the relative complexity of the work. DCLG-3 (5 points) covers overdue-date and rate calculation plus posting to the fine ledger, while DCLG-5 (5 points) includes payment handling, ledger update and restoration of borrowing privileges. DCLG-4 (3 points) is smaller because it mainly presents the outstanding fine transactions. Planning Poker would help the team validate these relative estimates and discuss uncertainty before sprint commitment.

2. Was your backlog well-prioritized?

Yes. All three stories were set to High priority because they form the core overdue-fine member flow and directly affect the member's account balance and borrowing privileges. The backlog was also scheduled logically: calculate and post the fine first, provide visibility of the outstanding transaction next, and then enable payment and balance restoration. Priority was therefore set at story level.

3. How did your simulated sprints align with your plan?

Both sprints aligned with the plan. Sprint 1 delivered 8 points across DCLG-3 and DCLG-4, while Sprint 2 delivered the remaining 5 points in DCLG-5. Across the two one-week sprint time-boxes, all 13 planned story points and all 3 stories under the Overdue Fine Management epic were completed without scope creep.

4. What insights did the burndown chart give about your team's capacity?

The burndown charts show committed work reducing from 8 to 0 points in Sprint 1 and from 5 to 0 points in Sprint 2. This confirms that the team completed 100% of the planned workload within the one-week sprint time-boxes. The results indicate that the planned capacity was achievable for this backlog, while a longer real project with daily progress tracking would provide a stronger basis for measuring velocity.

Overall observation

The exercise reinforced that story scope, priority, estimation and sprint commitment should be decided before execution. The Jira board and reports provided a clear trace from backlog planning through two one-week sprint time-boxes and final completion, while the burndown charts showed whether the planned workload was achieved.
